


Lawrence Berkeley National Lab Capital Projects

Presentation to Community Advisory Group

June 12, 2017


Building Construction and Demolition Map



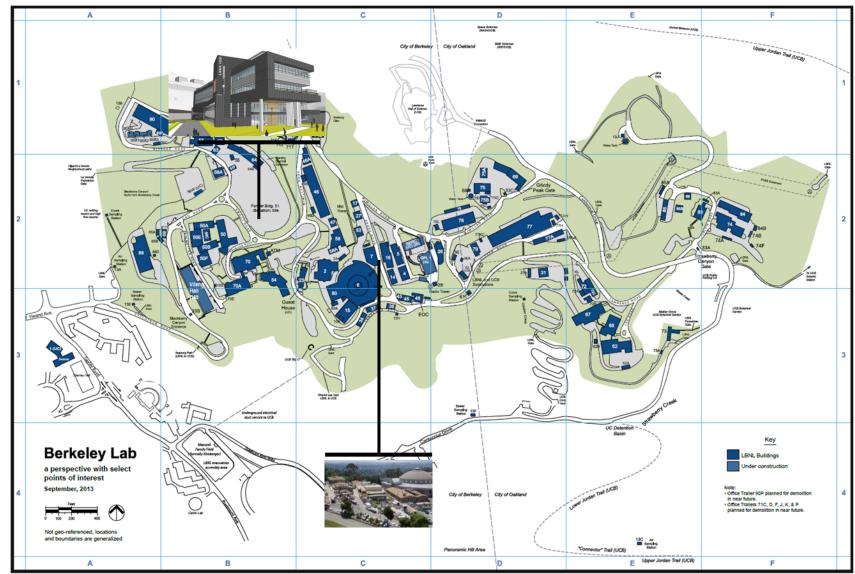

Old Town Demolition Phase 1



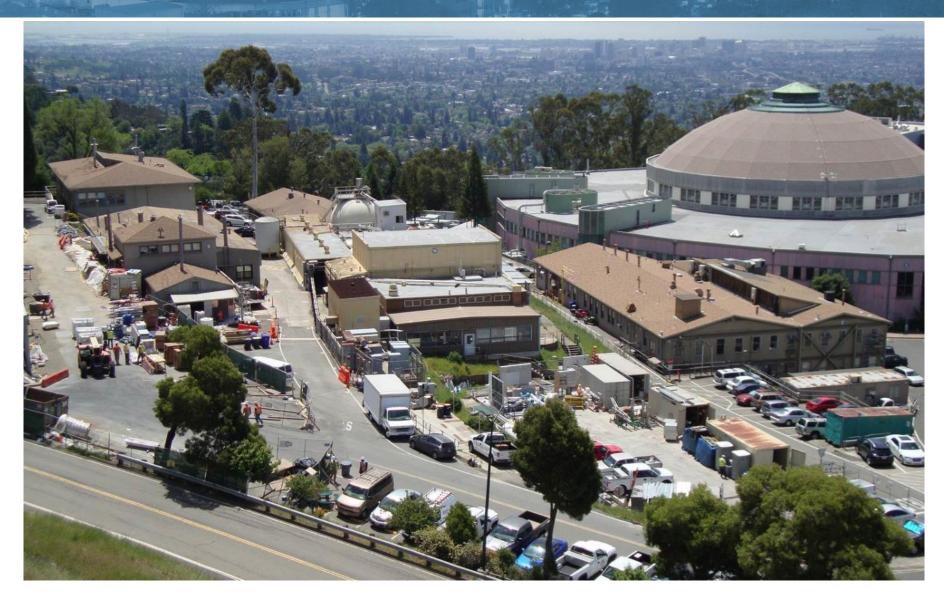

Old Town Demo Phase 1: Project update



- Finished project completion criteria for Old Town Phase I in May
- Beginning Phase I project closeout activities
- Developing planning documents for Phase II, Buildings 4, 7, 7C, and 14
- Initiating Phases III and IV to address remnant issues near Buildings 5, 16, 52, and 52A that are beyond Phase I scope, e.g.:
 - PCB contamination near Building 52A
 - PCB contamination west of Building 16
 - Removal of Building 16/16A retaining wall and Perkins Pad slab



Old Town Demo Phase 1





Old Town Demo Phase 1







Old Town Demo Phase 1





IGB: Perspective from northwest





IGB: Status



- Current planned construction completion is December 2018, move planned to take 6 months
- Micropile foundation 100% complete and test results accepted.
- Grade beam work ~ 10% complete.
- Shop drawing submittals for MEP systems underway
- Foundation construction expected to complete in July.


























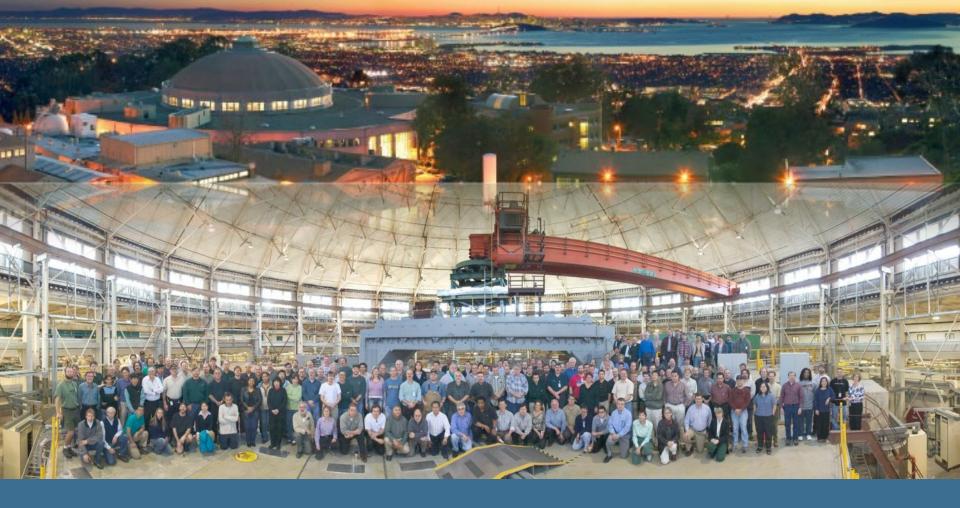

Thank You

Find us at: www.lbl.gov
