


Lawrence Berkeley National Lab Capital Projects

Presentation to Community Advisory Group

September 14, 2015

Building Construction Map



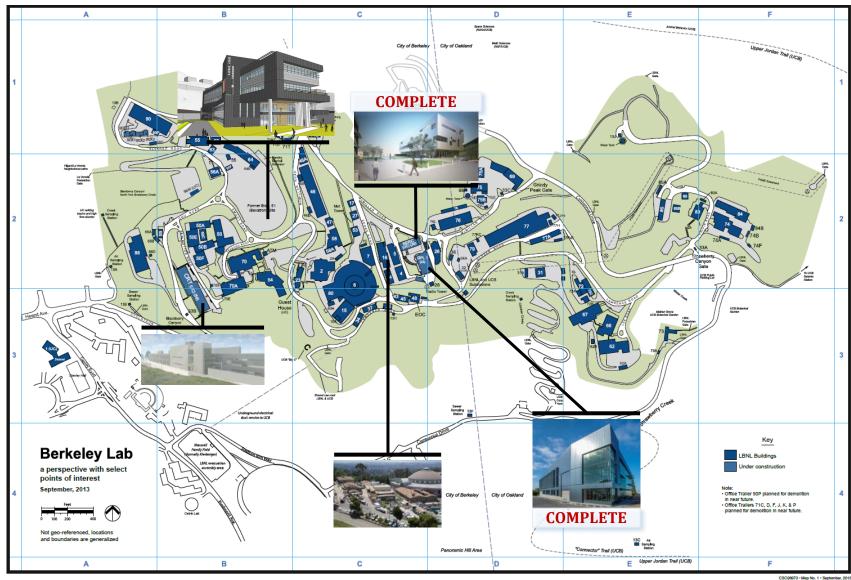

Solar Energy Research Center (SERC)






SERC – Current Activities





SERC – Current Activities



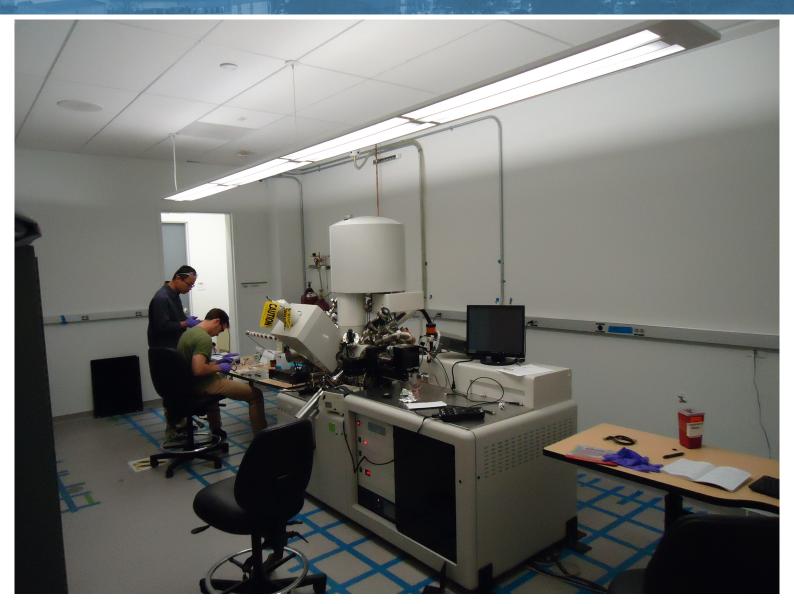

General Purpose Laboratory (GPL)





GPL – Current Activities






GPL – Current Activities






Computational Research and Theory Facility (CRT)



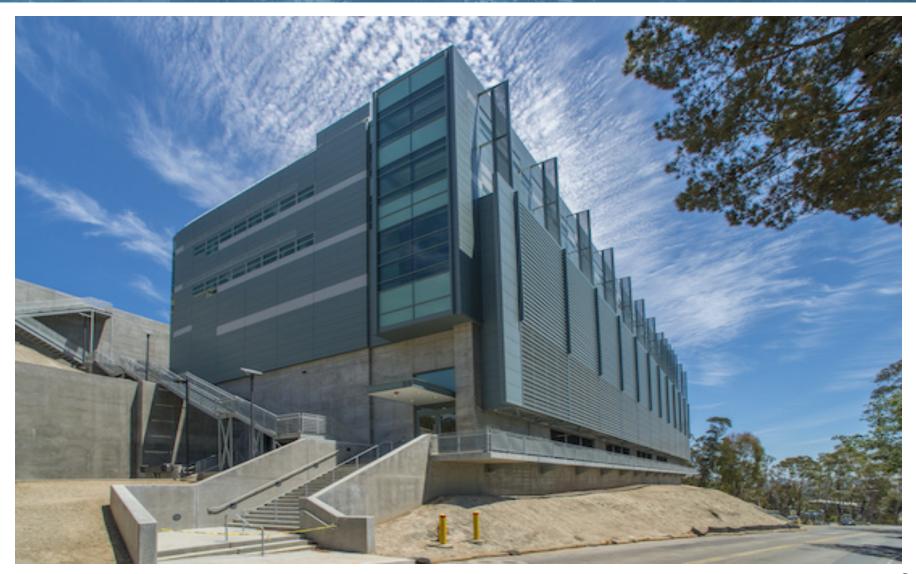

Computational Research and Theory Facility (CRT) – Current Activities



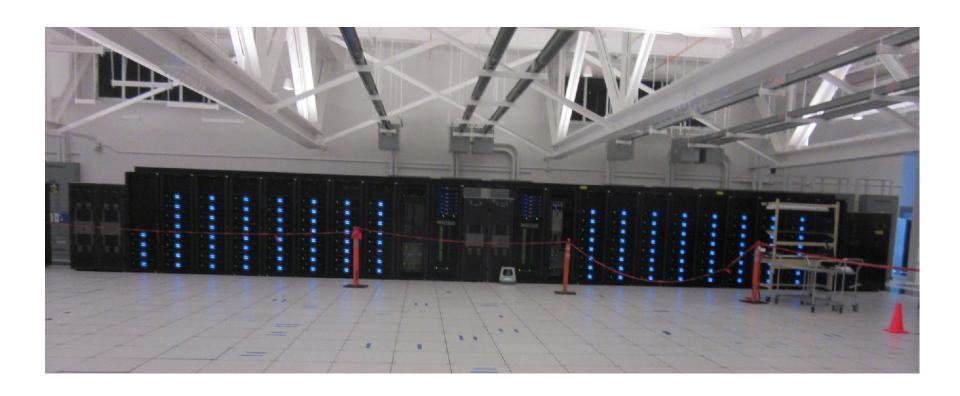


Old Town Demolition (OTD)





Old Town Demolition (OTD)



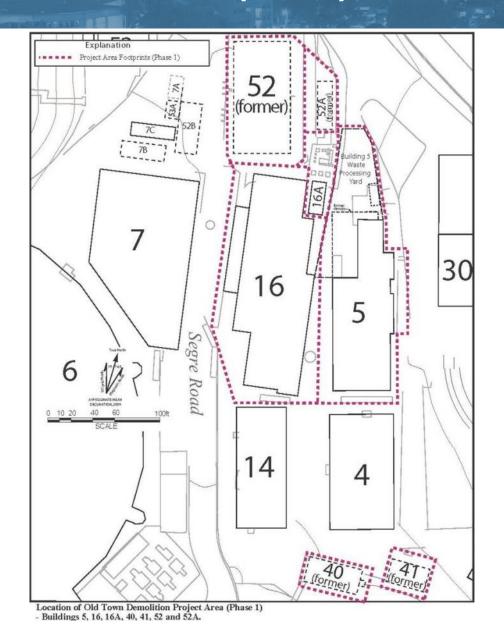

Old Town Demolition (OTD) - Current Activities



- Contract awarded to Dynamic Management Solutions (DMS) December 1, 2014
- Preparedness review held May 19-20, 2015
- Notice to Proceed issued June 5, 2015
- Subcontractor mobilization is complete
- B5 utility isolations, universal waste removal, and lead abatement/stabilization are done
- Low-level PCB contamination found at OT site, removal is being managed in close coordination with EPA
- B16 utility isolations, universal waste removal, and lead abatement/stabilization are working
- B5 asbestos abatement will complete Sep 2015
- B5 structure demolition will complete Oct 2015
- Phase I completion expected Summer 2016



Integrative Genomics Building (IGB)






IGB -Current Activities



- CEQA approved by Regents last June
- Completed review of the Schematic Design. 50% Design Development currently being reviewed
- CD-2 IPR scheduled for Nov 17 19. Preparatory Director's Review scheduled for Oct. 13 and 14
- Rudolph & Sletten selected for CM/GC contract. They constructed Foundry
- Complete Construction Documents on schedule for March 2016
- Early Start construction Summer 2016
- Estimate 24 months of construction
- IGB Early Finish construction complete ~ Fall 2018

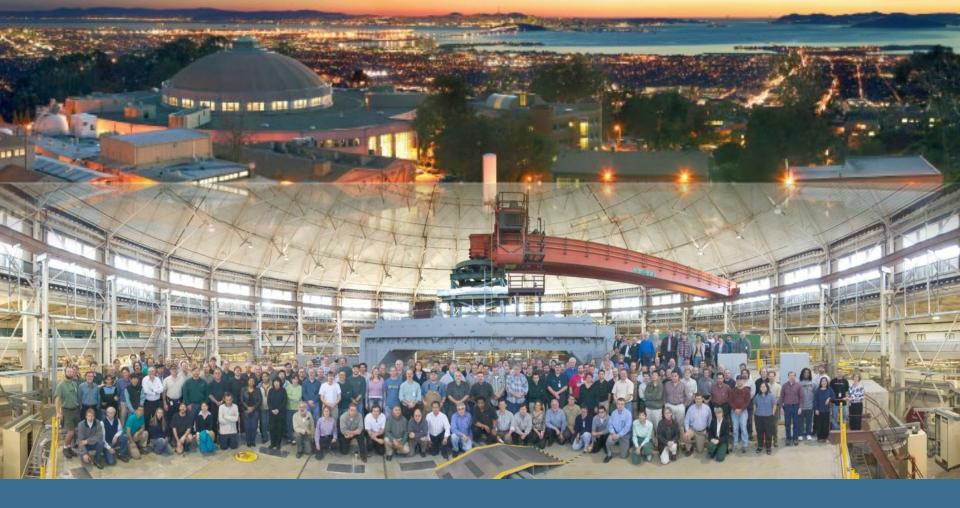

Thank You

Find us at: www.lbl.gov
