


Lawrence Berkeley National Lab Capital Projects

Presentation to Community Advisory Group

June 13, 2016

Building Construction and Demolition Map



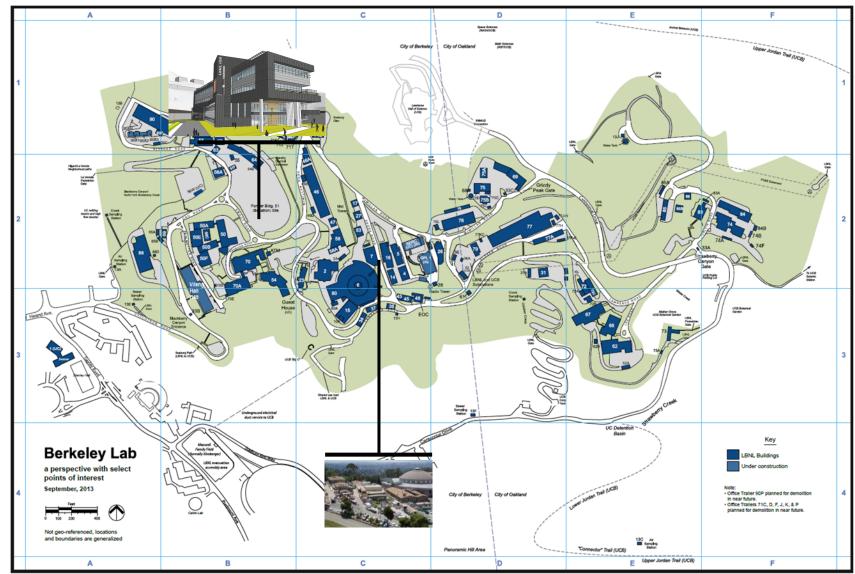


Old Town Demolition Phase 1





Old Town Demolition Phase 1



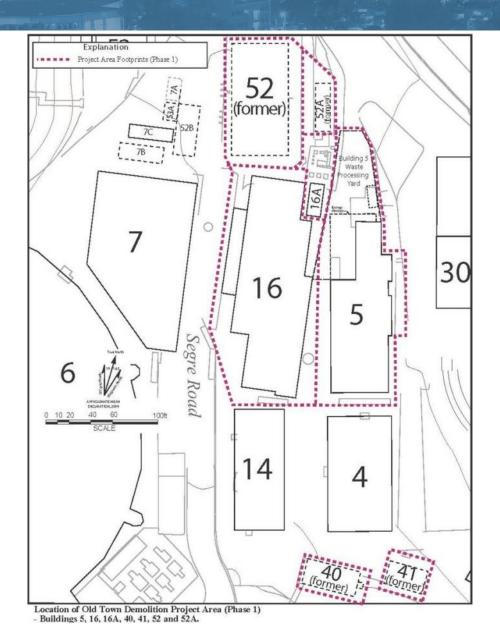

Old Town Demo Phase 1: Project update



- Removal of low-level radioactive waste processing yard slabs, utilities, soils completed
- Redesign of new B5 yard retaining wall extension completed; installation in progress
- Packaging and shipping of soils continuing
- Filtration of collected stormwater in progress
- Cleanup of PCB contamination in soils near B52/ B52A areas expected to begin this month
- Phase I completion expected in 4-7 months



Old Town Demo Phase 1





Old Town Demo Phase 1





Old Town Demo Phase 1





IGB: Perspective from northwest






IGB: Status



- Subcontractor bids have been received and budget documents sent to DOE
- DOE has scheduled a meeting on October 7, 2016 for final review and approval of construction plan
- Anticipate construction to take approximately 24 to 30 months completing in November 2018
- Move in to the building will take approximately 6 months

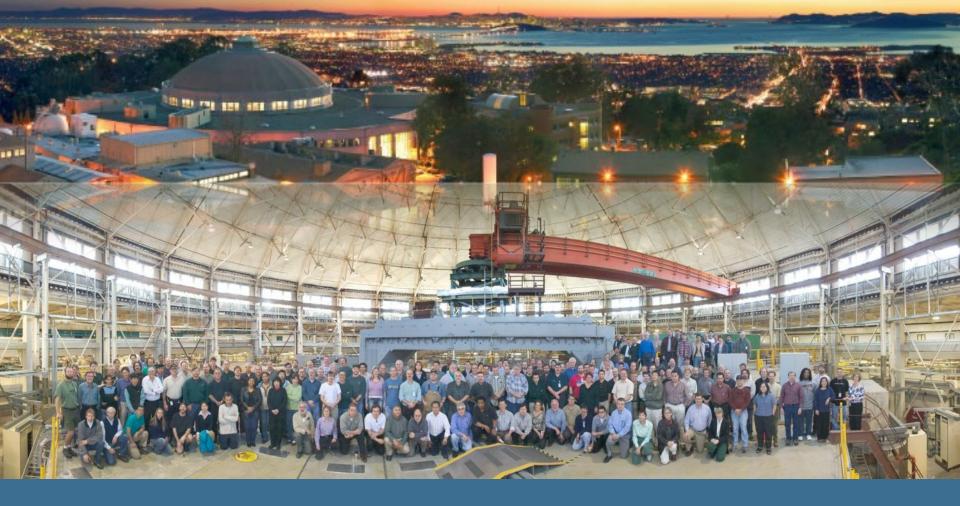

Thank You

Find us at: www.lbl.gov
