



Lawrence Berkeley National Lab Capital Projects

Presentation to Community Advisory Group

January 23, 2017




Old Town Demolition Phase 1



Old Town Demo Phase 1: Project update



- Removal of low-level radioactive waste from Building 5, along with associated utilities and soils completed
- Packaging and shipping of soils from Building 5 substantially complete
- Filtration of collected stormwater on going
- Cleanup of PCB contamination in soils near B52/B52A areas has begun
- Work planning for the cleanup of Building 16 slabs and soils is underway
- Phase I completion expected in 3-6 months

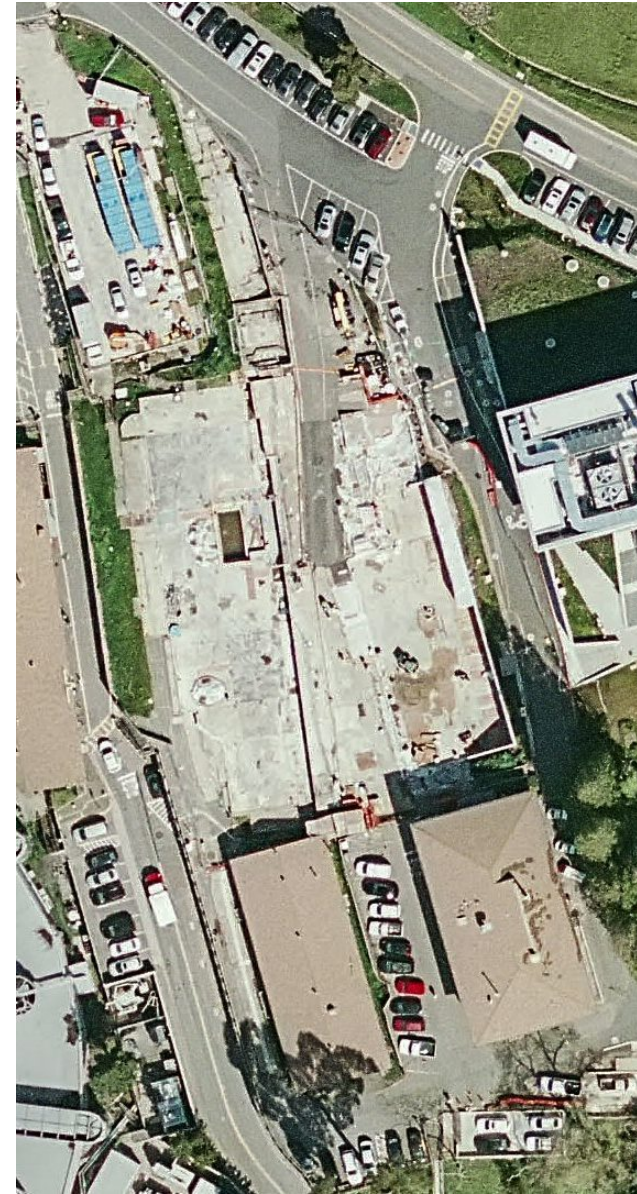

Old Town Demo Phase 1



Old Town Demo Phase 1



Old Town Demo Phase 1



IGB: Perspective from northwest



IGB: Status



- DOE approved the start of construction on Oct. 7, 2016
- Construction contract was awarded and Notice to Proceed was provided to Rudolph and Sletten (R&S) on Oct. 28, 2016
- Anticipate construction to take approximately 24 to 30 months completing in November 2018
- Move in to the building will take approximately 6 months

IGB Site



IGB Site



IGB Site



IGB Site



IGB Ongoing Activities



- “Big Room” up and running
- Project team fully mobilized on site
- Existing asphalt demo complete
- Subgrade preparation activities ongoing
- Micropile foundation installation underway ~ 345 total
 - Progressing from west to east
 - 2 rigs at a rate of 10 per day
- Foundation grade beams, pile caps, and elevator pit to follow
- SWPPP best management practices installed



Thank You

Find us at: www.lbl.gov
